

AMERICAN EAGLE FIRE PROTECTION, INC.

4711 North Dixie Highway – Boca Raton, FL 33431

Telephone: 561-750-3698 – Fax: 561-750-8496

LIC # 33490800012003


FLOW TEST

STATIC PRESSURE (psi)	RESIDUAL PRESSURE (psi)	PITOT PRESSURE (psi)	PITOT FLOW (gpm)	OUTLET SIZE
66	62	32	946	2"

Address: 872 E. McNab Road, Pompano Beach, FL

Flow Test Date: Tuesday, May 21, 2024 at 8:00 a.m – Wednesday, May 22, 2024 at 7:30 a.m.

Sketch of Test Location

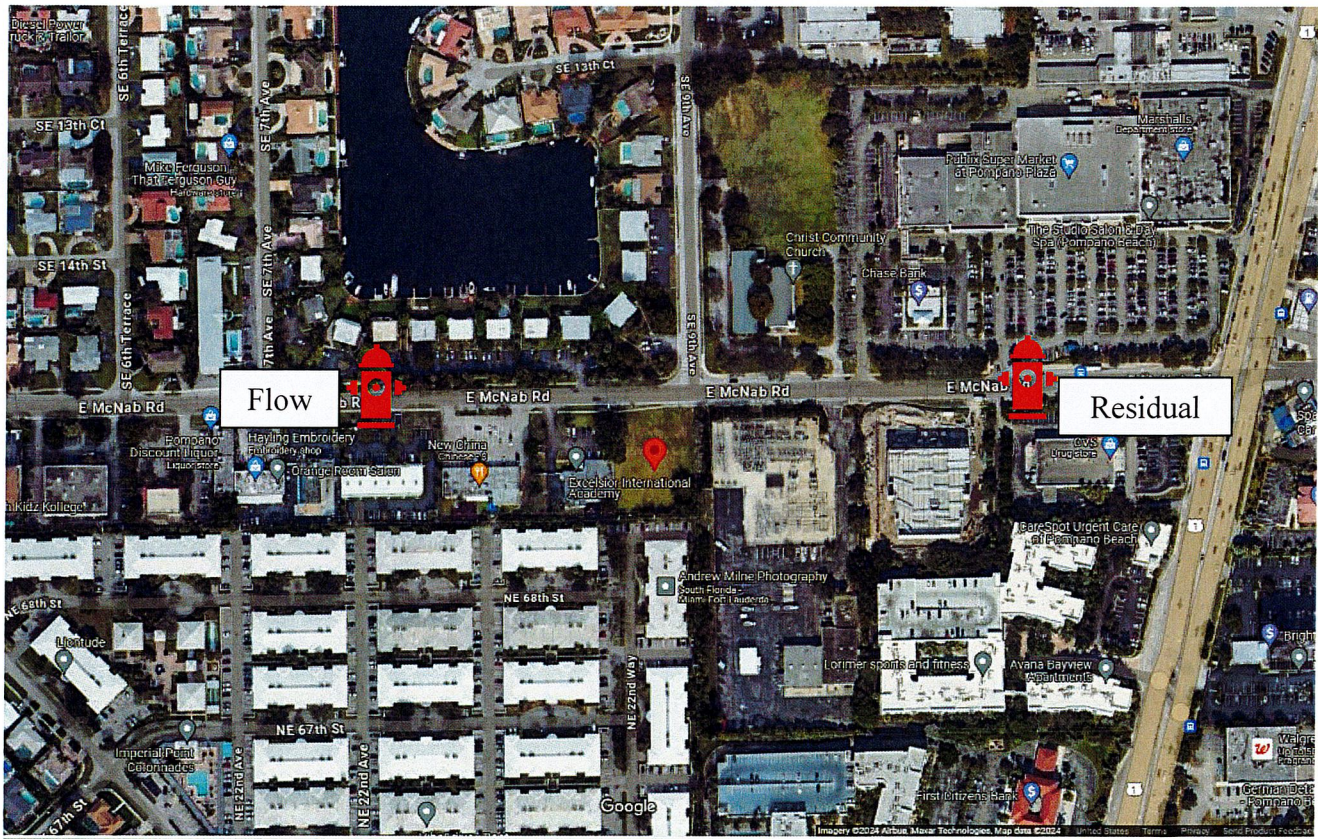

X Dario Cimetta

Date 65-22-24

AAC

PZ23-12000045

12/16/2024



Fire Prevention Fire Hydrant Flow Test



City of Pompano Beach • Bureau of Fire Prevention
100 West Atlantic Boulevard, Room 220 Pompano Beach, FL 33060
Phone: (954) 786-4695

City of Pompano Beach Fire Prevention will **WITNESS** all fire hydrant flow test that are required for fire flow purposes.

- City of Pompano Beach Code of Ordinances Title IX Chapter 95 Section 95.14(G). Fire hydrant flow tests.
 - The Fire Department shall witness all hydrant flow tests as required for fire protection systems.
 - All fire flow tests shall be in accordance with NFPA 291 and Broward County Amendments F-112.
 - Broward County Amendments F-112(e) - The static pressure at the water main shall be determined by a recorded method for a minimum twenty-four (24) hour period.
 - Morning of fire Hydrant static/residue connection contractor to provide documents of test equipment certification.

Information:

Date:	5-16-2024
Company Requesting Flow Test:	American Eagle Fire Protection, Inc.
Contact Name:	Elizabeth Hearon/ Adam Summers
Contact Phone Number:	561-750-3698 / 561-756-5864
Email Address:	salesassistant@americaneagflp.com
Associated Application Number:	
Associated Project Name:	872 E. McNab Road.

Proposed Date/Time for Fire Hydrant Flow Test: (8am – 9am)

- Request Hydrant Flow Test minimum 72 hours in advance.
- Connection of Fire Hydrant for 24 hour static/residual must be between 0730hrs and 0830hrs.

Requested Date:	Tuesday, May 21, 2024	Time:	8:00 a.m.
Alternate Date:	Wednesday, May 22, 2024	Time:	

Fire Hydrant Flow Test Location: 872 McNab Road, Pompano Beach, FL

Hydrant Location - Static/Residual:	
Hydrant Location - Flow:	

Fire Hydrant Flow Test Witness Fee:

There is a \$150.00 fee for performing each flow test. All tests will be completed within 5 business days. Please include map/sketch showing streets/cross streets & locations of flow and residual fire hydrants. Return flow test application to the Bureau of Fire Prevention with form of payment for \$150.00.

Make check and money orders payable to "CITY OF POMPAN0 BEACH"
If mailing in application with payment send to the addressed listed below.

Pompano Beach Fire Prevention
100 W. Atlantic Blvd. – Room 220
Pompano Beach, FL 33060

NOTE TO TREASURY: Post to 001-0000-367.30-00

	Yes	No				
Flow Test Equipment Certification:			Date:			
Fire Hydrant Id	Flow Pitot PSI	Flow GPM	Static Pressure 24 hr. Low PSI	Static Pressure Before Flow	Residual PSI During Flow	Tip Size
Total Hydrant Flow:						

- Fire Flow Data to be completed and entered on site.
- Fire flow data provided to Fire Prevention at a later date, must be signed/sealed by the Engineer of Record.

Person Conducting Flow Test:

Fire Inspector Witnessing Flow Test:
