
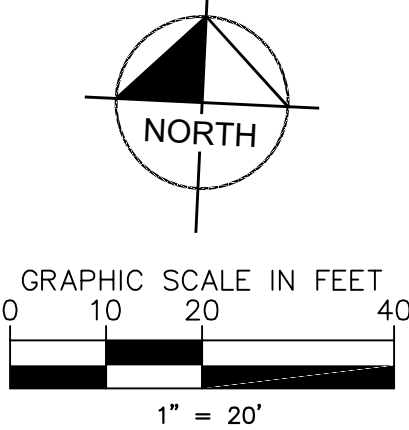


Plotted By: Milodon, Teresa Sheet Set: BREWERY LAYOUT: C101 DEMOLITION & EROSION CONTROL PLAN June 20, 2023 06:38:29pm K:\FTL\GVA\044\Jobs\044203010-Cypress Nook\CAD\PlanSheet - Brew Fish Brewery\C101 DEMOLITION & EROSION CONTROL PLAN.dwg
This document, together with the concepts and designs presented herein, is an instrument of service, as an instrument of service, is intended only for the specific purpose and client for which it was prepared. Reuse of and improper reliance on this document without written authorization and adaptation by Kimley-Horn and Associates, Inc. shall be without liability to Kimley-Horn and Associates, Inc.

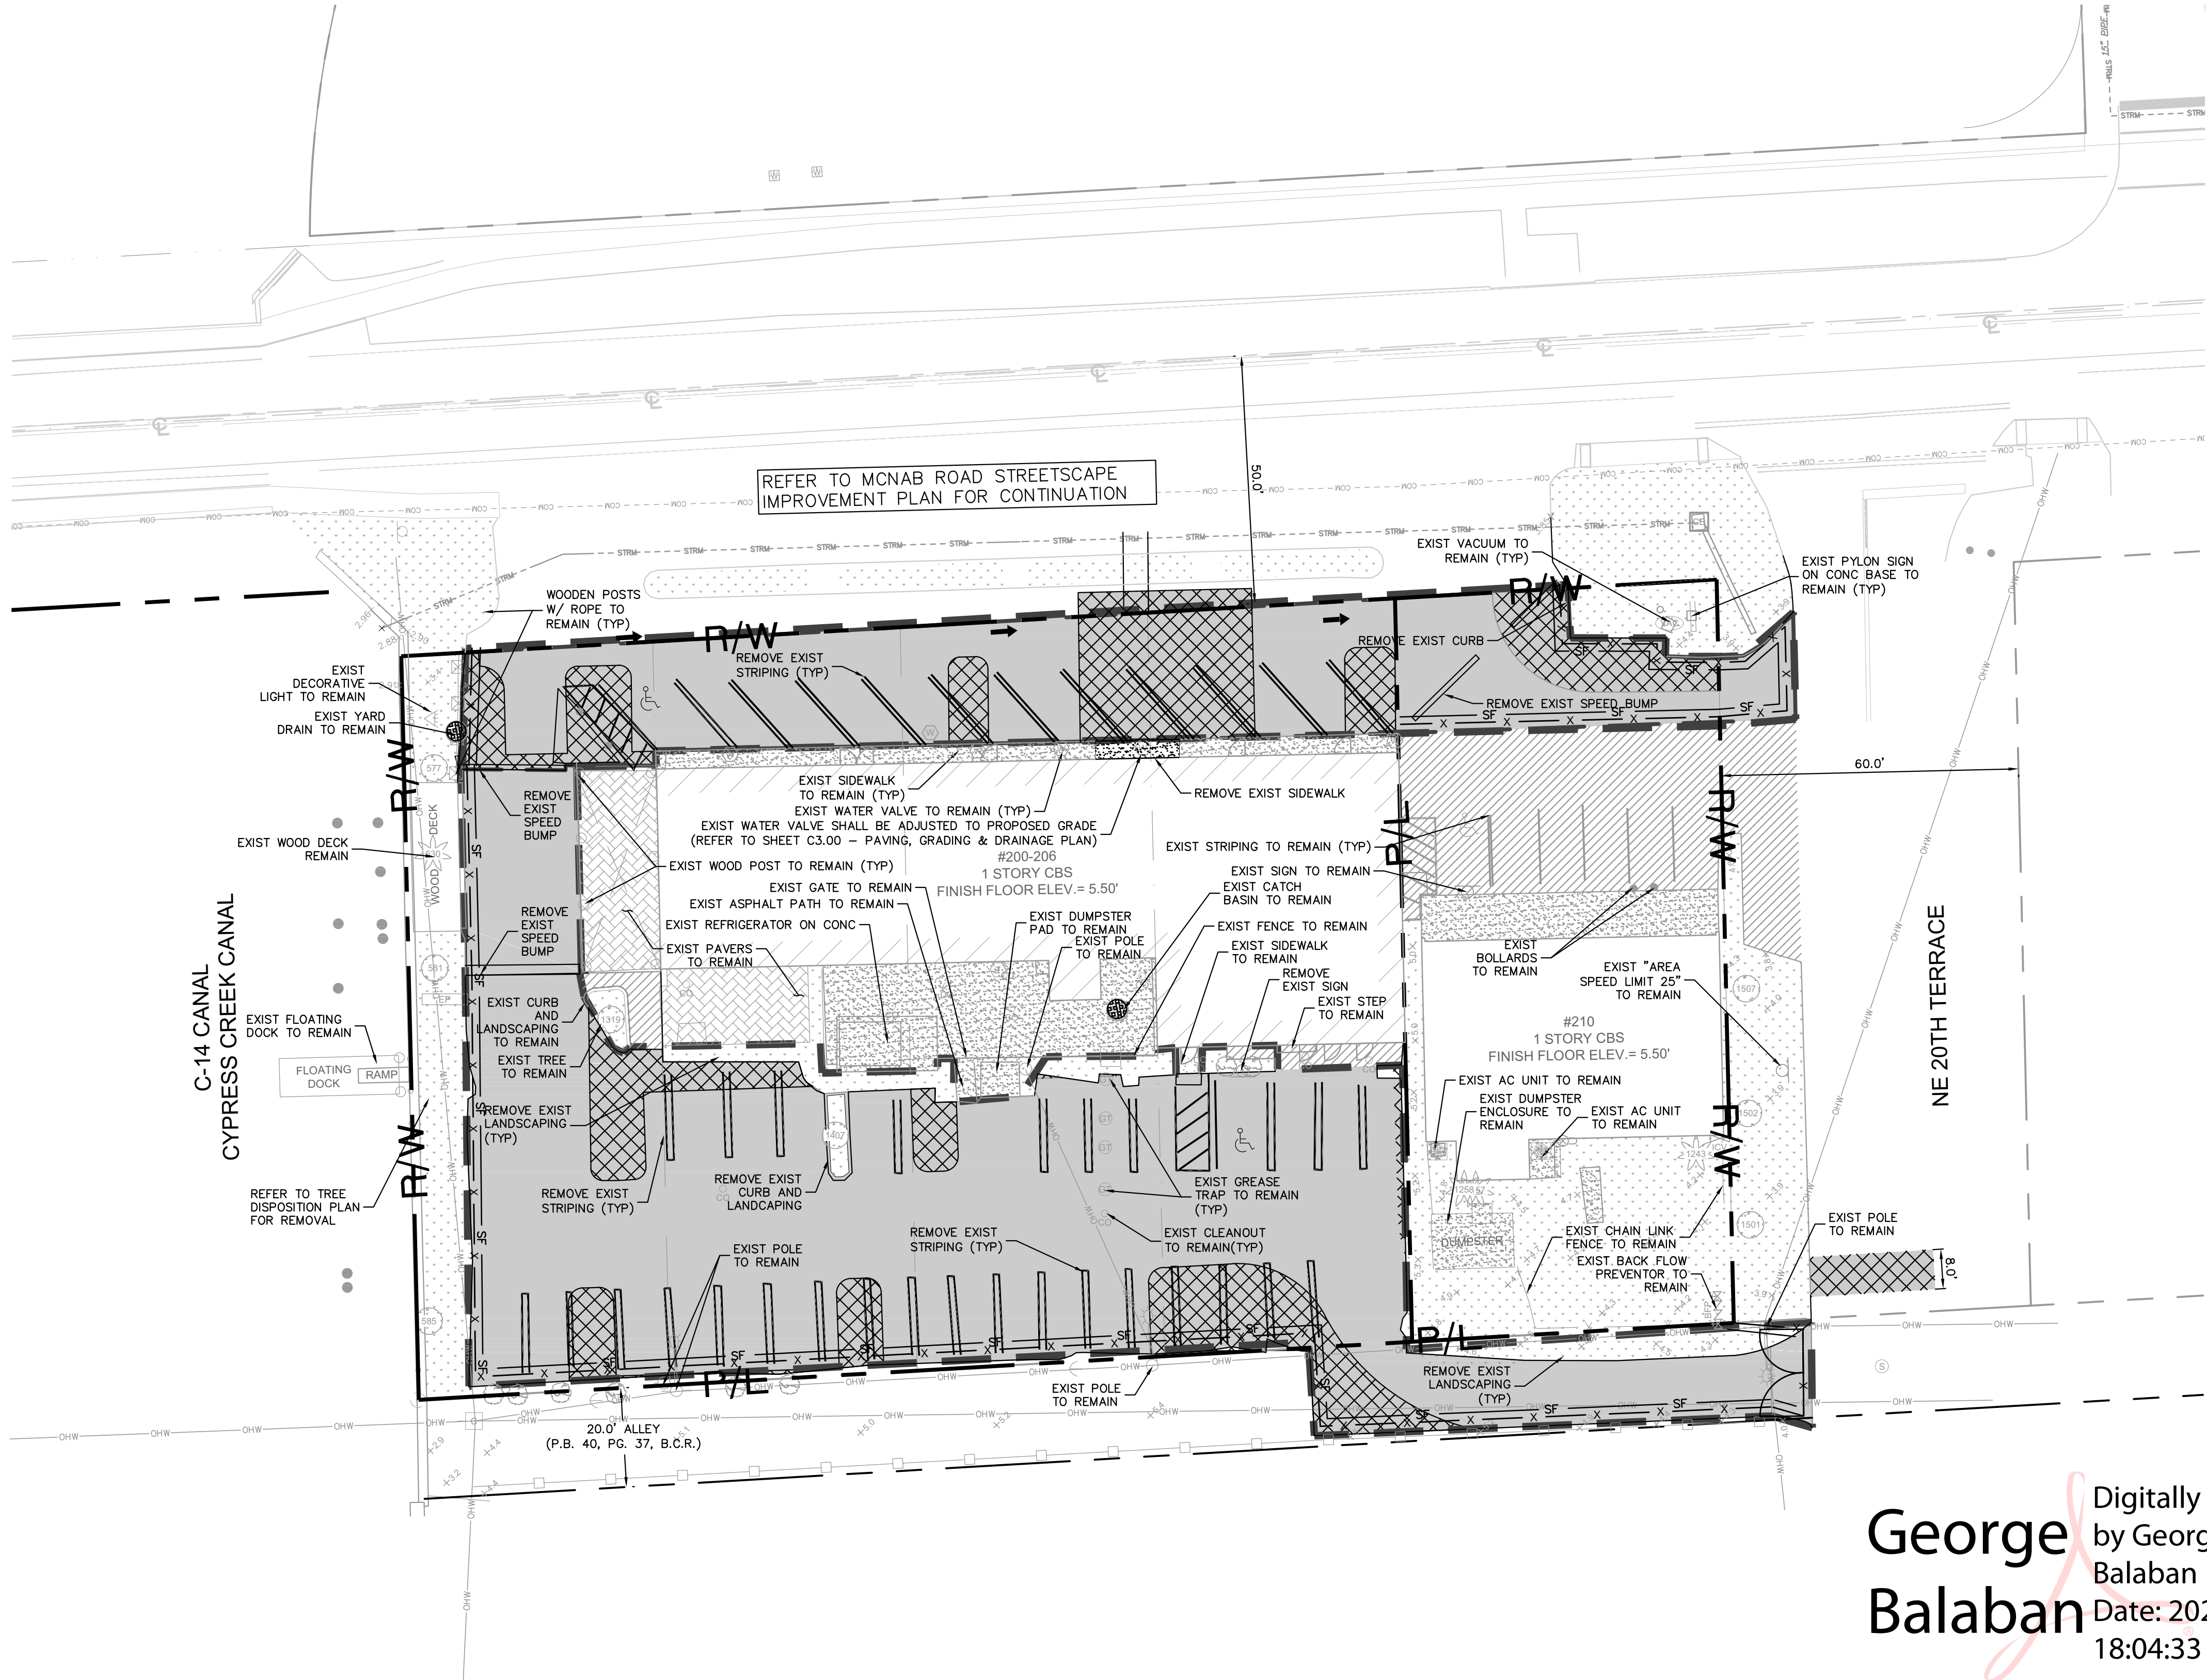

LEGEND

- CENTER LINE OF ROADWAY
- PROPERTY LINE AND/OR RIGHT-OF-WAY
- PROP SILT FENCE SEDIMENT CONTROL
- PROP 6' CHAIN LINK CONSTRUCTION FENCE WITH POLES AT 10'-0" O.C. AND VISUAL DUST SCREEN
- TURBIDITY BARRIER
- FILTER SACK
- FULL DEPTH ASPHALT PAVEMENT REMOVAL
- LIMITS OF 1" MILL AND RESURFACE
- EXIST ASPHALT TO REMAIN
- EXIST CONCRETE TO REMAIN
- EXIST CONCRETE REMOVAL
- EXIST PAVERS TO REMAIN
- EXIST OVERHEAD ELECTRIC
- EXIST OVERHEAD ELECTRIC POLE
- LIMITS OF DEMOLITION

EROSION CONTROL NOTES:

- STOCKPILED MATERIAL SHALL NOT BE LEFT IN EROSION PRONE AREAS UNLESS PROTECTED BY COVER OR ROCK BAGS.
- DUMPSTER ARE REQUIRED TO BE COVERED WHEN NOT EMPTYING OR FILLING.
- SEE SHEET C1.02 FOR EROSION CONTROL DETAILS.
- CONTRACTOR TO RELOCATE CONSTRUCTION FENCE AND SILT FENCE TO BE WITHIN PROPOSED PROPERTY LINES AFTER PROPOSED DEMOLITION AND RIGHT-OF-WAY IMPROVEMENTS ARE COMPLETED.
- INSTALL AND MAINTAIN DUST SCREENS ON THE INSIDE OF THE PROPOSED CONSTRUCTION FENCE IN ORDER TO PREVENT OBSTRUCTION ON TO NEIGHBORING PROPERTIES.
- EXISTING UTILITIES TO REMAIN AND BE PROTECTED AT ALL TIMES.
- CONTRACTOR TO REFER TO LANDSCAPE PLANS FOR ANY REQUIRED TREE PROTECTION DETAILS.

DEMOLITION NOTES:

- INFORMATION ON THIS PLAN IS BASED ON THE SURVEY PROVIDED BY KEITH, DATED 03/04/2022.
- THE INTENT OF THE DEMOLITION PLAN IS TO DEPICT ALL EXISTING FEATURES THAT ENCUMBER THE PROPOSED CONSTRUCTION, AND ARE SCHEDULED FOR REMOVAL. SOME INCIDENTAL ITEMS MAY HAVE BEEN OMITTED FROM THE PLAN. THE CONTRACTOR SHALL THOROUGHLY INSPECT THE SITE AS WELL AS REVIEW THE PLANS AND SPECIFICATIONS PRIOR TO SUBMITTING PRICING. CONTRACTOR WILL NOT RECEIVE ADDITIONAL COMPENSATION FOR INCIDENTAL ITEMS NOT SHOWN ON THIS DEMOLITION PLAN.
- SEE LANDSCAPE PLANS FOR TREES TO REMAIN, BE REMOVED, RELOCATED, OR PROTECTED.
- ALL MODIFICATIONS, REMOVALS AND RELOCATIONS OF EXISTING UTILITIES SHALL BE COORDINATED WITH THE UTILITY OWNER PRIOR TO CONSTRUCTION.
- CONTRACTOR TO SAWCUT AND MATCH EXISTING WHEN CONNECTING TO ADJACENT PAVEMENT.
- IF REQUIRED, CONTRACTOR TO COORDINATE WITH THE CITY OF POMPANO BEACH TO OBTAIN AN APPROVED MAINTENANCE OF TRAFFIC PLAN FOR VEHICULAR AND PEDESTRIAN TRAFFIC PRIOR TO COMMENCING WORK.
- DO NOT BLOCK OR OBSTRUCT FIRE HYDRANTS AT ANY TIME. PROVIDE CERTIFIED FIRE EXTINGUISHERS ONSITE.
- IF ASBESTOS MATERIALS ARE ENCOUNTERED, THE CONTRACTOR IS TO PREPARE, AS REQUIRED, ALL NECESSARY ABATEMENT AS PER ENVIRONMENTAL REGULATIONS.
- CONTRACTOR SHALL VISIT JOB SITE AND PHYSICALLY SURVEY ALL OF THE AS-BUILT CONDITIONS TO ASCERTAIN THE FULL SCOPE OF CLEARING AND DEMOLITION WORK. IF CONDITIONS ARE ENCOUNTERED OTHER THAN THOSE SHOWN ON THIS PLAN, THE CONTRACTOR SHALL NOTIFY THE ENGINEER PRIOR TO PROCEEDING WITH WORK.
- ANY GRAFFITI OR UNAPPROVED SIGNS THAT SHOW UP ON THE CONSTRUCTION FENCE OR JOBSITE SHALL BE REMOVED IMMEDIATELY.
- INSTALL AND MAINTAIN DUST SCREENS ON THE INSIDE OF THE PROPOSED CONSTRUCTION FENCE IN ORDER TO PREVENT OBSTRUCTIONS TO THE SIDEWALK SHOULD THEY COME LOOSE.
- CONTRACTOR SHALL SEEK CITY APPROVAL FOR ANY PUBLIC SIDEWALKS AND/OR STREETS TO BE CLOSED DURING CONSTRUCTION.
- CONTRACTOR SHALL ENSURE PROPER EROSION CONTROL IS IN PLACE PRIOR TO DEMOLITION.

George Balaban
Digitally signed by George Balaban
Date: 2023.06.22 18:04:33 -04'00'

GEORGE BALABAN, STATE OF FLORIDA, PROFESSIONAL ENGINEER, LICENSE NO. 74543

THIS ITEM HAS BEEN DIGITALLY SIGNED AND SEALED BY GEORGE BALABAN, P.E. ON THE DATE INDICATED HERE.

PRINTED COPIES OF THE DOCUMENT ARE NOT CONSIDERED SIGNED AND SEALED AND THE SIGNATURE MUST BE VERIFIED ON ANY ELECTRONIC COPIES.

PLANS ARE IN NAVD 1988 DATUM
CONVERSION EQUATION IS BELOW:
(NAVD 1988) + 1.58' = (NGVD 1929)

THE PRESENCE OF GROUNDWATER SHOULD BE ANTICIPATED. CONTRACTOR'S BID SHALL INCLUDE CONSIDERATION FOR ADDRESSING THIS ISSUE AND OBTAINING ALL NECESSARY PERMITS.

Always call 811 two full business days before you start to dig to have underground utilities located and marked.

Sunshine 811.com

223-12000029.01

09/20/2023

Kimley»Horn

© 2023 KIMLEY-HORN AND ASSOCIATES, INC.
8201 PETERS ROAD, SUITE 2200, PLANTATION, FL 33324
PHONE: 954-535-5100 FAX: 954-739-2247
WWW.KIMLEY-HORN.COM REGISTRY No. 35106

LICENSED PROFESSIONAL
DATE: JUNE 2023
SCALE: AS SHOWN
DESIGNED BY: TVC
DRAWN BY: TVC
CHECKED BY: GB
DATE: _____

DEMOLITION &
EROSION CONTROL
PLAN

BREW FISH
BREWERY
PREPARED FOR
CITY OF POMPANO BEACH
FL

BREW FISH
BREWERY
PREPARED FOR
CITY OF POMPANO BEACH
FL

SHEET NUMBER
