

DRC

DATA FLOW TEST

DRC

PZ22- 12000027
12/03/2025

PZ22-12000027

07/02/2025

EF20000738


FPC15-000086


SYMMETRIK INC.
FIRE PROTECTION & SECURITY SYSTEMS

HYDRANT # & LOCATION: 2900 Sample Road - Festival Market DATE: 11/6/2019
TEST BY: Joe/Heather Day or Week: Tues TIME OF DAY: 8:44 MIN. OF FLOW: 5
WATER SUPPLIED BY: Municipal
PURPOSE OF TEST: New construction

DATA

FLOW HYDRANT(S)	A1	A2	A3
SIZE OPENING:	<u>2.5</u>	<u> </u>	<u> </u>
COEFFICIENT:	<u>0.9</u>	<u> </u>	<u> </u>
PITOT READING:	<u>45</u>	<u> </u>	<u> </u>
GPM:	<u>1126</u>	<u> </u>	<u>0</u>
TOTAL FLOW DURING TEST:	<u>1126</u> GPM		
STATIC READING:	<u>71</u> PSI	RESIDUAL: <u>65</u> PSI	
RESULTS: AT 20 PSI RESIDUAL	<u>3575</u> GPM	AT 0 PSI	<u>4274</u> GPM
ESTIMATED CONSUMPTION:	<u>5628</u> GAL.		
REMARKS:			

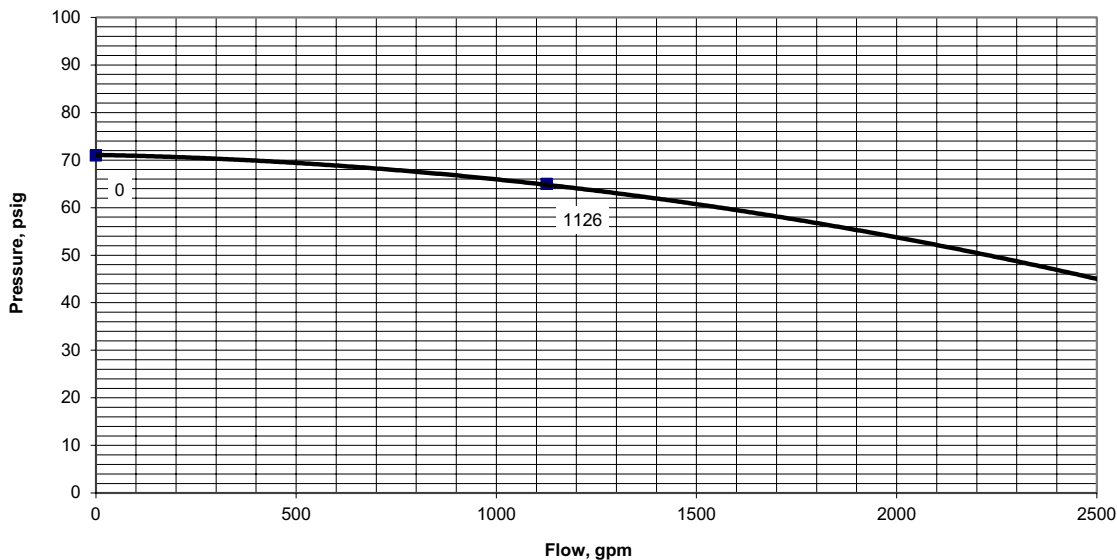

DRC

DRC

PZ22-12000027

10/01/2025

PZ22-12000027

10/5/2022
