

JMC Fire Protection Services Inc
5449 NW 24th Street Ste #4,
Margate, Florida, 33063.
Office: 954-973-8550
Fax: 954-973-6998

Fire Protection Contractor II #09560500012008

DRC

PZ24-12000020
03/18/2026

24 HOUR EMERGENCY SERVICE

FULL FLOW FIRE PUMP TEST

Date of Test: 5/6/2025


Work Order # 230621

Customer:	John Burkett	Inspector:	Jack D France Jr
Street:	701 S. Federal Hwy,	Also Present:	Kalicharan Jaikaran
City:	Pompano Beach, FL, 33062.		
Attn:	John Burkett		
Contact:	jburkert@pompanoboats.com 954-946-1450		

Page 1 of 1

Pump Information		Shaft		Manufacturer			Approved			Shop or Serial No.			Model Number					
		Yes	Horizontal	Data Plate on wall			Yes	Yes		K4HI-626762			2873A					
			Vertical					No										
		Gallons/Minute		Rated PSI		Net		Rated RPM		City Supply		Size Conn.		Tank Supply		Tank Height		
		750	GPM	65.2	PSI	44.5	PSI	3520	RPM		YES	4	Inch	No		N/A	Feet	
Driver Information		Manufacturer			Approved			Shop or Serial No.			Model Number			Horse Power		Rated RPM		
		US Electric Motors			Yes	Yes		B04S756A			S756A			40		H.P.	3525	RPM
						No												
		Elec. Motor?		Rated Volts		Oper. Volts		Rated Amps		Amps @ 150		Phase		Cycles		Service Factor		
		Yes			A.C.	208	A.C.	109	Amps		Amps	3	Phase	60	Hz	N/A		
Controller Information		Manufacturer			Approved			Fire Pump						Jockey Pump				
		Hubbell			Yes	Yes	On	88	PSI			On	149	PSI				
					No		Off	150	PSI	Yes	Auto	Off	150	PSI				
		Shop or Serial No.			Model Number													
		A946428-1-1			LX1200													
Revolutions Per Minute		Discharge Pressures		Suction Pressures		Net Pressures		Streams						GPM	%	Volts	Amps	
								Size	Pitot 1	Pitot 2	Pitot 3	Pitot 4	Pitot 5	Pitot 6				
3541	RPM	160	PSI	74	PSI	86	PSI	-	0	0	0	0	0	0	0	Churn	N/A	N/A
3520	RPM	115	PSI	55	PSI	60	PSI	1.75	13	13					756	1	N/A	N/A
3520	RPM	70	PSI	35	PSI	35	PSI	1.75	13	13	13				1134	1.5	N/A	N/A
	RPM		PSI		PSI		PSI											
	RPM		PSI		PSI		PSI											
	RPM		PSI		PSI		PSI											
	RPM		PSI		PSI		PSI											

Fire Pump Performance Test

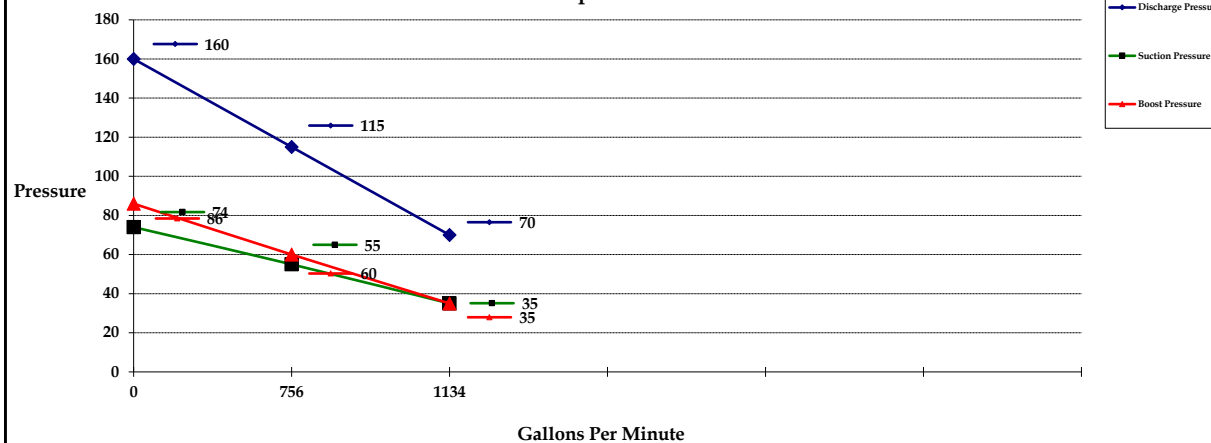

Comments:

Hose Monster equipment was calibrated June 2024.

Results Satisfactory? ☒ Yes
Date: 5/6/2025
