



Fire Prevention Fire Hydrant Flow Test



City of Pompano Beach • Bureau of Fire Prevention
100 West Atlantic Boulevard, Room 220 Pompano Beach, FL 33060
Phone: (954) 786-4695

City of Pompano Beach Fire Prevention will **WITNESS** all fire hydrant flow test that are required for fire flow purposes.

- City of Pompano Beach Code of Ordinances Title IX Chapter 95 Section 95.14(G). Fire hydrant flow tests.
 - The Fire Department shall witness all hydrant flow tests as required for fire protection systems.
 - All fire flow tests shall be in accordance with NFPA 291 and Broward County Amendments F-112.
 - Broward County Amendments F-112(e) - The static pressure at the water main shall be determined by a recorded method for a minimum twenty-four (24) hour period.
 - Morning of fire Hydrant static/residue connection contractor to provide documents of test equipment certification.

Information:

Date:	JULY 6, 2023
Company Requesting Flow Test:	GALLO HERBERT ARCHITECTS
Contact Name:	VICTOR JOHNSON
Contact Phone Number:	(954) 914-9280
Email Address:	VICTOR.JOHNSON4006@YAHOO.COM
Associated Application Number:	
Associated Project Name:	FIBERBUILT UMBRELLA

Proposed Date/Time for Fire Hydrant Flow Test: (8am – 9am)

- Request Hydrant Flow Test minimum 72 hours in advance.
- Connection of Fire Hydrant for 24 hour static/residual must be between 0730hrs and 0830hrs.

Requested Date:	JULY 11	Time:	9:00AM
Alternate Date:		Time:	

Fire Hydrant Flow Test Location:

Hydrant Location - Static/Residual:	SE CORNER OF NW 23 RD AVE. & NW 2 ND ST.
Hydrant Location - Flow:	NW 23 RD AVE. JUST N OF ATLANTIC BLVD.

Fire Hydrant Flow Test Witness Fee:

There is a \$150.00 fee for performing each flow test. All tests will be completed within 5 business days. Please include map/sketch showing streets/cross streets & locations of flow and residual fire hydrants. Return flow test application to the Bureau of Fire Prevention with form of payment for \$150.00.

Make check and money orders payable to "CITY OF POMPANO BEACH"
If mailing in application with payment send to the addressed listed below.

Pompano Beach Fire Prevention
100 W. Atlantic Blvd. – Room 220
Pompano Beach, FL 33060

NOTE TO TREASURY: Post to 001-0000-367.30-00


	Yes	No	
Flow Test Equipment Certification:	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Date: 7/6/23

Fire Hydrant Id	Flow Pitot PSI	Flow GPM	Static Pressure 24 hr. Low PSI	Static Pressure Before Flow	Residual PSI During Flow	Tip Size
	45	1130				
			52	80	75	
Total Hydrant Flow:						

- Fire Flow Data to be completed and entered on site.
- Fire flow data provided to Fire Prevention at a later date, must be signed/sealed by the Engineer of Record.

VICTOR JOHNSON
Person Conducting Flow Test:

JASON CONGER
Fire Inspector Witnessing Flow Test:

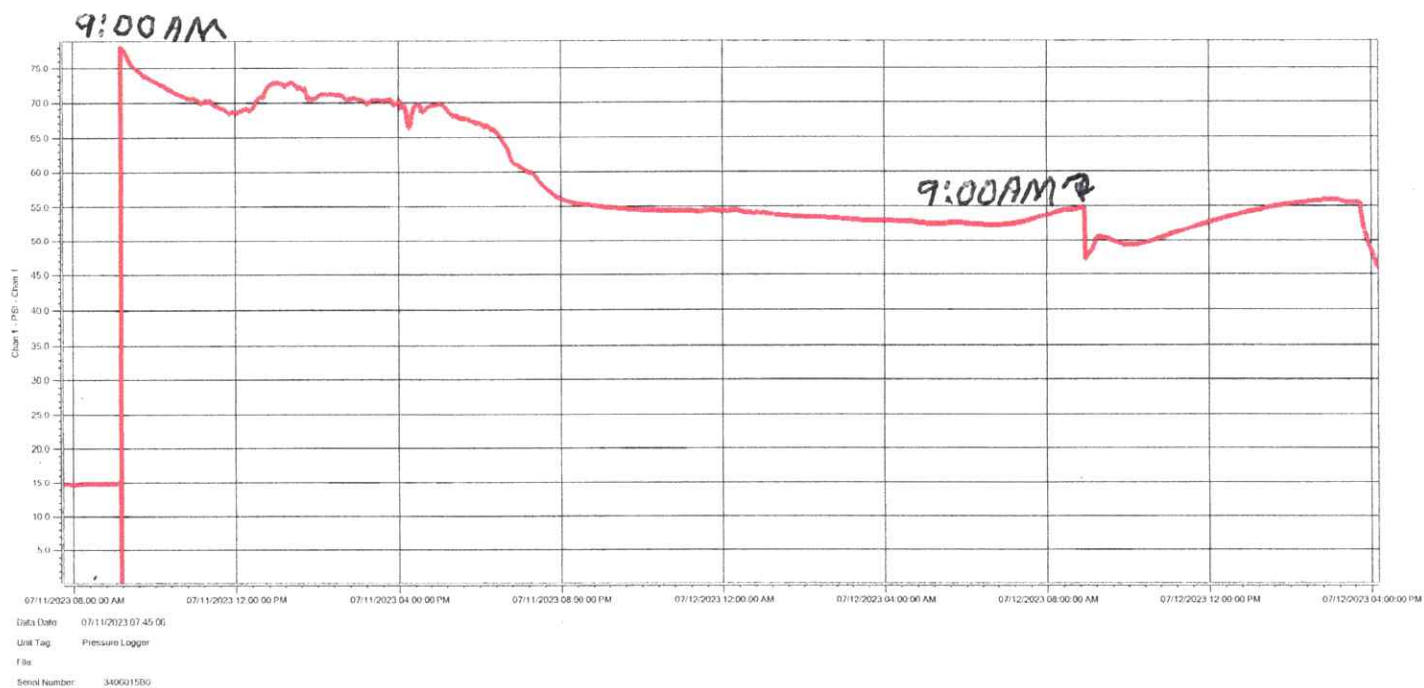

DRC

PZ21-12000052
03/06/2024
