

POMPANO PARKWAY - STATE ROAD #845  
(POWERLINE ROAD - S.W. 25th. AVENUE)

EROSION CONTROL NOTES:

THE ESCAPE OF SEDIMENT FROM THE SITE SHALL BE PREVENTED BY THE INSTALLATION OF EROSION AND SEDIMENT CONTROL MEASURES AND PRACTICES PRIOR TO, OR CONCURRENT WITH, LAND DISTURBING ACTIVITIES.

SITE EROSION CONTROLS SHALL BE CHECKED AND IF NECESSARY, REPAIRED WEEKLY AND WITHIN 24 HOURS AFTER EACH RAINFALL  $\geq 1/2"$ . IN THE EVENT OF CONTINUOUS RAINFALL, EROSION CONTROLS SHALL BE CHECKED DAILY.


EROSION AND SEDIMENTATION CONTROL MEASURES WILL BE MAINTAINED AT ALL TIMES. ADDITIONAL EROSION AND SEDIMENTATION CONTROL MEASURES AND PRACTICES WILL BE INSTALLED AS DEEMED NECESSARY BY ONSITE INSPECTION.

ALL EROSION CONTROL MEASURES ARE TO CONFORM TO THE STANDARDS SET FORTH IN THE USDA "PLANNING AND DESIGN MANUAL FOR EROSION AND SEDIMENT CONTROL", AND THE FLORIDA DEPARTMENT OF ENVIRONMENTAL PROTECTION (FDEP) "STORMWATER BMP MANUAL FOR BEST MANAGEMENT PRACTICES", CURRENT EDITIONS.


ALL AREAS TO REMAIN BARE > 15 DAYS MUST BE TEMPORARILY STABILIZED.

WASTE MATERIALS SHALL NOT BE DISCHARGED TO WATERS OF THE STATE.

INSPECTIONS: CONTRACTOR SHALL INSPECT AND DOCUMENT EROSION AND SEDIMENT CONTROL MEASURES AND REPAIR AS NEEDED MIN. 2 TIMES PER WEEK AND AT LEAST 72 HOURS APART.

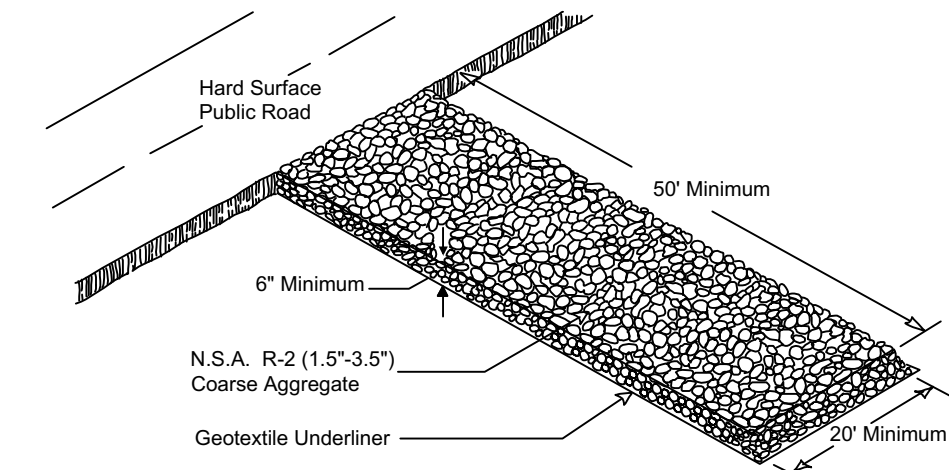

Co CRUSHED STONE CONSTRUCTION EXIT

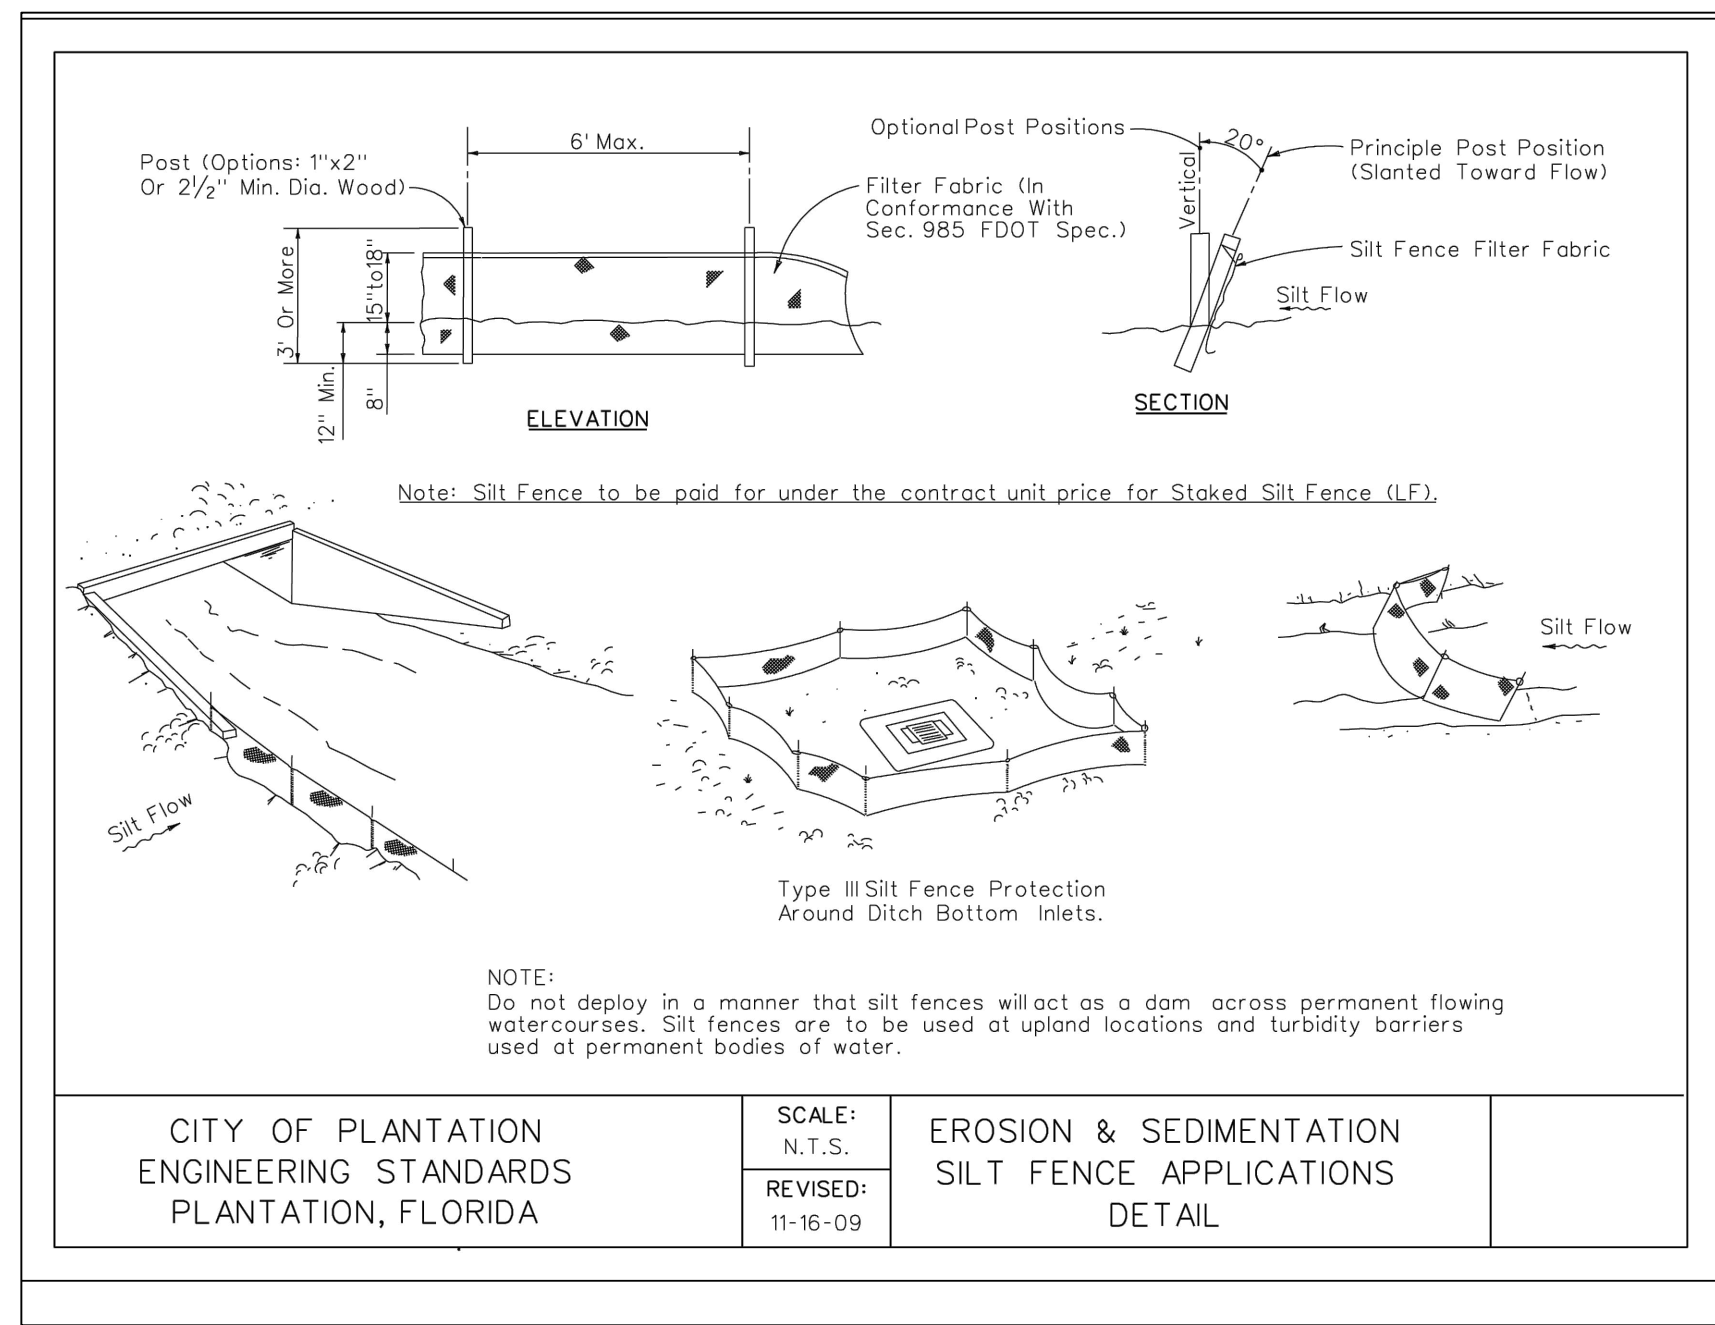

Sd1 SILT FENCE DETAIL  
NO SCALE

GENERAL NOTES:

CONSTRUCTION MATERIALS, ASSEMBLIES AND PROCEDURES ARE TO FOLLOW:

- LOCALLY ADOPTED BUILDING CODES AND SUPPLEMENTARY ORDINANCES. WHEN A CONFLICT OCCURS BETWEEN SUCH LOCAL CODES AND INFORMATION SHOWN ON THE PLANS CONSULT ENGINEER OF RECORD FOR RESOLUTION PRIOR TO COMMENCING WORK. CONTRACTOR IS TO NOTIFY ENGINEER OF RECORD IF SITE CONDITIONS.
- OR DIMENSIONS DISAGREE WITH INFORMATION SHOWN ON THE DRAWINGS. WORK IS NOT TO PROCEED UNTIL SUCH DIFFERENCES ARE RESOLVED.
- DRAWINGS SHALL NOT BE SCALED. "NOT TO SCALE" (INDICATED AS N.T.S.) AND THE LISTED DIMENSIONS GOVERN.
- EACH CONTRACTOR SHALL BE RESPONSIBLE FOR REPAIR OR DAMAGE TO THE WORK OF EACH OF THE OTHER TRADES CAUSED BY HIS OPERATIONS. REPAIR WORK MUST RECEIVE THE PRIOR APPROVAL OF THE COMPANY REPRESENTATIVE. THE CONTRACTOR IS RESPONSIBLE FOR LOCATING ALL EXISTING UTILITIES.
- AND FOR PROTECTING THEM FROM DAMAGE. THE CONTRACTOR SHALL BEAR THE COST OF REPAIR OR REPLACEMENT TO UTILITIES DAMAGED BY THE CONTRACTOR. G.C. SHALL PROVIDE EROSION CONTROL/SEDIMENTATION BARRIER (HAY BALES OR SILTATION CURTAIN) TO PREVENT SILTATION OF ADJACENT PROPERTY, STREETS, STORM SEWERS, AND WATERWAYS. INGRESS AND EGRESS TO SITE, DURING CONSTRUCTION, IS ALLOWED ONLY.
- THROUGH APPROVED SITE DRIVEWAYS.



LOCATION MAP  
1" = 100'

CLIENT:




DESIGN TEAM TITLE:

MDM  
SERVICES, INC.

engineering • environmental • construction

2151 W. HILLSBORO BLVD, DEERFIELD BEACH,  
FLORIDA 33442  
Phone: (954) 427-3076  
FLORIDA CA #4857

NO. DATE REVISION DESCRIPTION



Digitally signed by Daimian D. Leslie  
Date: 2023.06.28  
15:05:13-0400'

DAIMIAN D. LESLIE  
FL REG # 73113

PROJECT DESCRIPTION:

NEW  
C-STORE

SITE DESIGNATION:

SUNSHINE GASOLINE DISTRIBUTORS  
CHEVRON  
GAS STATION #010

SITE ADDRESS:

301 POMPANO PKWY,  
POMPANO BEACH, FL  
33069

SCALE: AS NOTED MDW JOB # 21119

DATE: 08-11-2022

DESIGNED BY:

DRAWN BY: FILE NAME:

CHECKED BY: 21119 CD.DWG

DRAWING TITLE:

EROSION CONTROL  
PLAN

SHEET NO.:

DRC  
EC 1.0



Know what's below.  
Call before you dig.

Copyright © MDM SERVICES, INC.

All rights reserved. No part of this plan may be reproduced, distributed, or transmitted in any form or by any means, including photocopying, recording, electronic or mechanical methods, without the prior written permission of MDM Services, Inc. For permission requests, write MDM Services, Inc., 1055 Kathleen Road, Lakeland, FL 33809.

PZ22-12000038  
08/16/2023
