Dixie Hwy Segment 3A - Baseline / GMP

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	Total Float
Milestones						
S-1000	3A-NE 10th St to Copans Rd - Overall Constuction Duration (Calendar Days)	546	546	26-Feb-25	25-Aug-26	0
MS-0001	Construction Start	0	0	26-Feb-25		72
IMP-MS-0001	Impacted Construction Start after Seg 2 FEC Work	0	0	15-Aug-25		0
MS-3A999	NE 10th St to Copans Rd Complete	0	0		08-Jun-26	0
*A1010	Substantial Completion	0	0		25-Aug-26	0
*A1070	Final Completion	0	0		23-Dec-26	0
Preconstruction						
PC-1000	50% Drawings Issued by Design Team	0	0	01-Feb-22 A		
PC-1010	WT Issues Draft GMP/Constructability Comments based on 50% Drawings To City/EOR	35	0	02-Feb-22 A	23-Aug-22 A	
PC-2032	Design Team Issues 90% Drawings	10	0	02-Feb-22 A	20-Nov-23 A	
PC-1020	City/EOR Review 50% Budget and Constructability Comments for Final drawing Revisions	20	0	24-Aug-22 A	30-Aug-22 A	
PC-2042	City Negotiates Agreement with FEC (Target=2/25/25)	520	126	02-Feb-23 A	25-Feb-25	2
PC-2034	WT Submits 90% Drawings to Bldg Dept for Permit	16	0	21-Nov-23 A	19-Mar-24 A	
PC-1040	WT Issues Final Budget based on 100% Drawings	15	2	01-Feb-24 A	27-Aug-24	111
PC-2036	WT Issue RFI to Design Team (90%)	20	0	20-Mar-24 A	07-Aug-24 A	
PC-1050	City/EOR Review and Approve Budget	10	10	28-Aug-24	11-Sep-24	111
PC-1060	City Commission 1 st reading	1	1	13-Sep-24*	13-Sep-24	111
PC-1070	City Commission 2nd reading	1	1	26-Sep-24*	26-Sep-24	103
PC-1080	City Legal Submits Ordinance / NTP 1 (Allows WT to issue PO's & Subcontracts	51	51	27-Sep-24	10-Dec-24	103
PC-2042.1	IMPACT:Segment 2 FEC Procurement Complete	77	77	26-Feb-25	16-Jun-25	2
PC-2042.2	IMPACT: Segment 2 FEC Work	40	40	17-Jun-25	12-Aug-25	2
Permitting						
PC-1032	Permit Cycle 1 90 % Drawings Building Department Issues Comments	10	0	04-Dec-23 A	04-Dec-23 A	
PC-1030	Permit Cycle 1 EOR Issues 90% Drawings	10	0	20-Mar-24 A	26-Mar-24 A	
PC-1090	Permit Cycle 2 EOR Issues 100% Drawings for Permitting	10	0	27-Mar-24 A	01-Apr-24 A	
PC-1100	Permit Cycle 2 WT Submits 100% Drawings to City Building Department Permit Review	5	0	02-Apr-24 A	09-Apr-24 A	
PC-1110	Permit Cycle 2 Building Dept Issue Comments 100% Drawings	15	0	10-Apr-24 A	10-Apr-24 A	
PC - 2000	City Issues Permit	1	0	14-Aug-24 A	14-Aug-24 A	
PC - 2010	WT and Subs Prepare to Mobilize to Site	10	10	26-Feb-25	11-Mar-25	72
Procurment						
Sub Awards						
SA1020	Award Contract to Civil Sub	10	10	11-Dec-24	26-Dec-24	152
SA1040	Award Contract to Flat Work Concrete	10	10	11-Dec-24	26-Dec-24	179
SA1060	Award Contract to SUE-Keith	10	10	11-Dec-24	26-Dec-24	103
SA1050	Award Contract to Landscape / Irrigation	10	10	27-Dec-24	10-Jan-25	241
SA1030	Award Contract to Electrical / Signalization	10	10	13-Jan-25	24-Jan-25	241
SA1070	Award Contract to Striping / Signage	10	10	27-Jan-25	07-Feb-25	315
Construction						
3A-1250	Schedule for Site Survey Utilities - 10th St to Sample	10	10	27-Dec-24	13-Jan-25	90
3A-1260	Site Survey Utilities - 10th St to Sample	10	10	14-Jan-25	29-Jan-25	90
NE 10th St to Copans Rd						

Start: 01-Feb-22
Finish: 23-Dec-26
Data Date: 24-Aug-24
Run Date: 24-Oct-24

Remaining Level of Effort
Critical Remaining Work
Actual Level of Effort
Milestone
Actual Work
Remaining Work

The Whiting-Turner Contracting Co.
Dixie Hwy Segment 3A - Baseline / GMP
DHWY3A-B00.1 GMP **All Activities** *1 of 2*

JS|HELD
WHITING-TURNER

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	Total Float
3A-1000	MOT-NE 10th to Copans	5	5	12-Mar-25	19-Mar-25	60
Median						
3A-1010	Demo Existing Median-NE 10th to Copans	20	20	20-Mar-25	17-Apr-25	60
3A-1020	Excavate for Curb-NE 10th to Copans	20	20	11-Apr-25	12-May-25	60
3A-1030	Start Form & Pour Curb-NE 10th to Copans	20	20	05-May-25	13-Jun-25	60
3A-1030.1	Complete Form & Pour Curb-NE 10th to Copans after FEC Seg 2	30	30	15-Aug-25	17-Oct-25	0
3A-1040	Excavate for Landscaping-NE 10th to Copans	45	45	20-Oct-25	08-Jan-26	62
3A-1050	Install Irrigation / Backfill-NE 10th to Copans	45	45	09-Jan-26	12-Mar-26	62
Northbound Outside Lane / Bke Lane						
3A-1060	MOT Shift to Northbound-NE 10th to Copans	5	5	20-Oct-25	28-Oct-25	0
3A-1070	Milling of Bike Lane-NE 10th to Copans	4	4	31-Oct-25	06-Nov-25	0
3A-1080	Excavate for D Curb-NE 10th to Copans	20	20	07-Nov-25	11-Dec-25	0
3A-1090	Form & Pour D Curb-NE 10th to Copans	25	25	02-Dec-25	12-Jan-26	0
3A-1092	Install Pedestrian Walks Signalization-NE 10th to Copans	10	10	13-Jan-26	26-Jan-26	0
3A-1180	Milling & Resurface-NE 10th to Copans	10	10	21-Apr-26	04-May-26	0
3A-1190	Striping-NE 10th to Copans	10	10	22-Apr-26	05-May-26	14
Southbound Concrete Flatwork						
3A-1100	MOT Shift to Southbound-NE 10th to Copans	5	5	27-Jan-26	02-Feb-26	0
3A-1110	Demo ADA Corners-NE 10th to Copans	15	15	03-Feb-26	23-Feb-26	0
3A-1170	Replace Existing Light & Bracket Arm-NE 10th to Copans (by FPL)	60	60	03-Feb-26	27-Apr-26	30
3A-1120	Form & Pour ADA Corners-NE 10th to Copans	30	30	17-Feb-26	30-Mar-26	0
3A-1130	Demo Bus Shelters / Concrete Pads-NE 10th to Copans	5	5	31-Mar-26	06-Apr-26	0
3A-1140	Form & Pour Bus Pads-NE 10th to Copans	5	5	07-Apr-26	13-Apr-26	0
3A-1150	Install Pedestrian Walks Signalization-NE 10th to Copans	5	5	14-Apr-26	20-Apr-26	0
3A-1160	Install Signage-NE 10th to Copans	10	10	21-Apr-26	04-May-26	25
3A-1200	Milling & Resurface-NE 10th to Copans	10	10	05-May-26	18-May-26	0
3A-1210	Temp Striping-NE 10th to Copans	10	10	06-May-26	19-May-26	14
3A-1240	Asphalt Cure Time-NE 10th to Copans (Calendar Days)	14	14	19-May-26	01-Jun-26	0
3A-1230	Thermo-Striping-NE 10th to Copans	5	5	02-Jun-26	08-Jun-26	0
Closeout						
A1000	Schedule Conting	55	55	09-Jun-26	25-Aug-26	0
A1010	Substantial Completion	0	0		25-Aug-26	0
A1050	Punchlist (Calendar Days)	60	60	26-Aug-26	24-Oct-26	0
A1060	Document Closeout (Calendar Days)	60	60	25-Oct-26	23-Dec-26	0
A1070	Final Completion	0	0		23-Dec-26	0

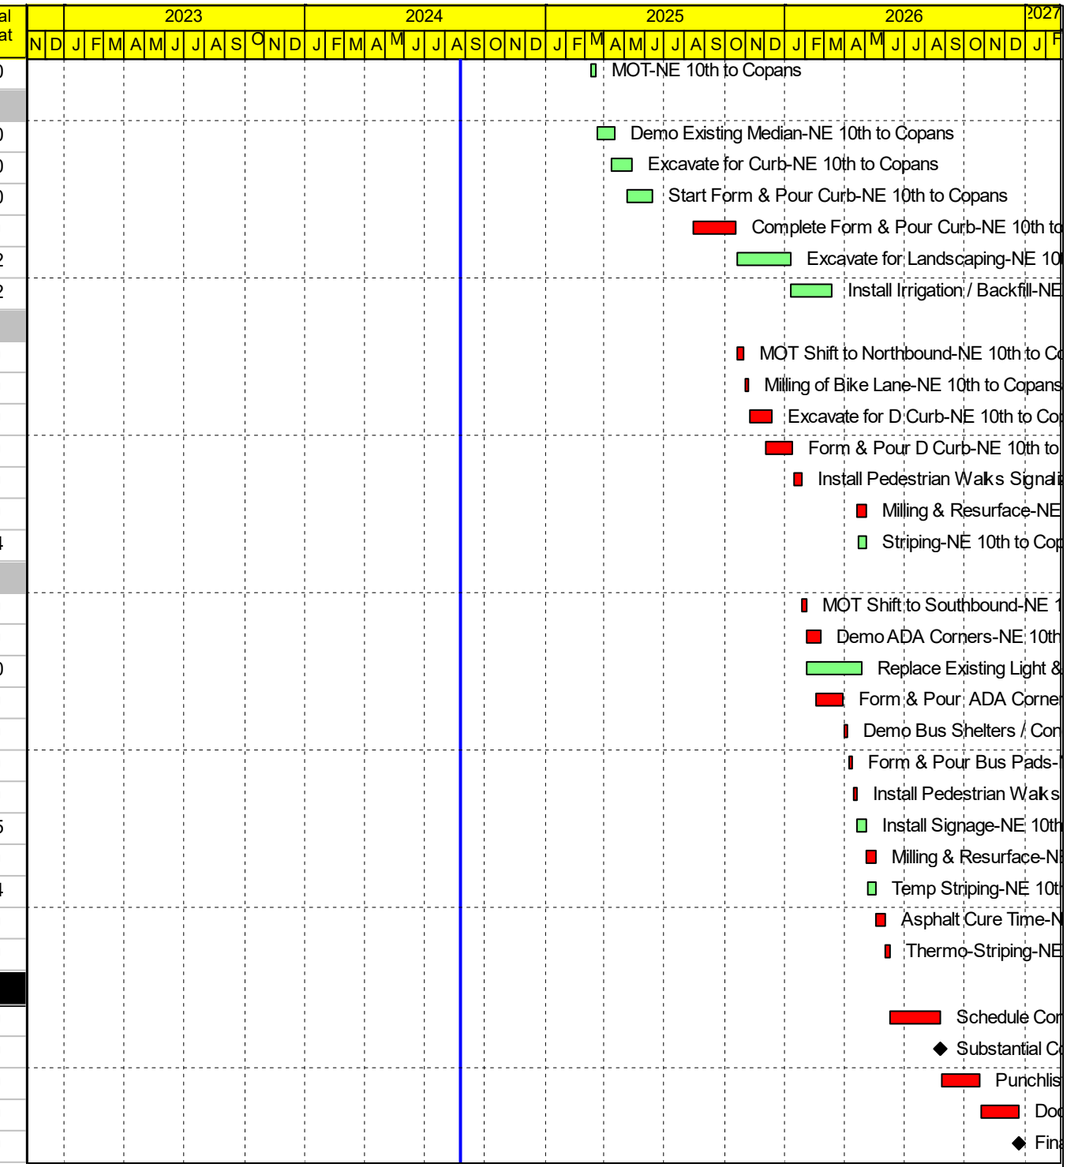

Start: 01-Feb-22
Finish: 23-Dec-26
Data Date: 24-Aug-24
Run Date: 24-Oct-24

Remaining Level of Effort
Critical Remaining Work
Actual Level of Effort
Milestone
Actual Work
Remaining Work

The Whiting-Turner Contracting Co.
Dixie Hwy Segment 3A - Baseline / GMP
DHWY3A-B00.1 GMP **All Activities** *2 of 2*

JS|HELD

WHITING-TURNER
